

TO: Jeannie Johnson,
JNU Airport Manager

DATE: July 6, 2010

FROM: Catherine Fritz, AIA
JNU Airport Architect

FILE: 1382.16

RE: Terminal Renovation Project Update


During this past month, work continued throughout the terminal with many different trades. The emphasis was toward completion of the secure-side toilet rooms and the new stairway. Unfortunately, neither of these was completed on time due to delays by the flooring subcontractor. However, airport operations were not severely disrupted and the Contractor is developing an acceleration plan to get back on schedule for the remaining work. Contract completion is currently scheduled for October, 2010.

The state elevator inspector is scheduled to be onsite for the final inspection of the new escalator on July 14. We expect to open the stairway by the same date.

JCVB began using their new space this week, and we are continuing to work with them to finish out the space with racks and storage systems that serve their needs.

The replacement carpeting is scheduled to arrive in late July, so several areas are expected to be occupied without the finished floor surfaces.

Efforts are now focused on the TSA Passenger Screening area on the second floor. Much of the mechanical and electrical work is complete in this area. Framing for the glass wall system is underway. A scene of the Mendenhall glacier and surrounding mountains will be fritted into the glass.

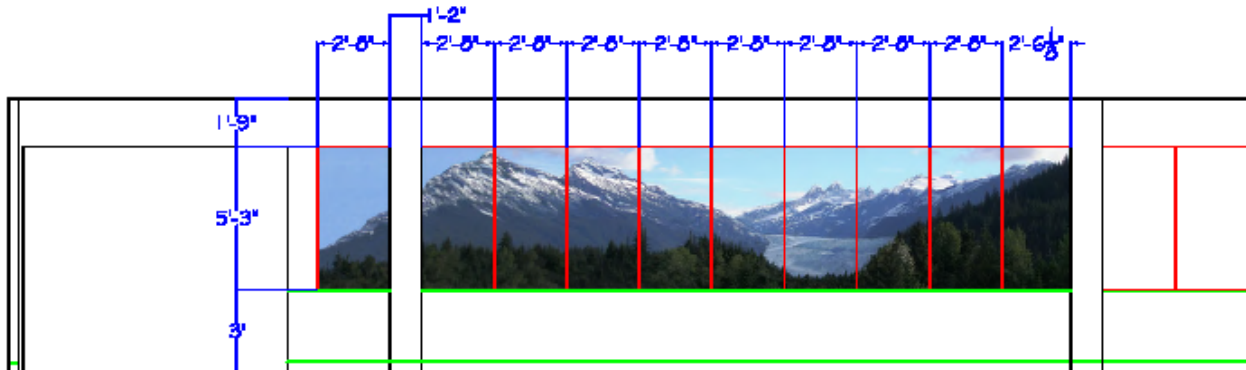

Mountain scene in fritted glass along TSA Screening walls.



Installing new drinking fountains in Departure Lounge.



Attaching guardrail system to new stairs.
